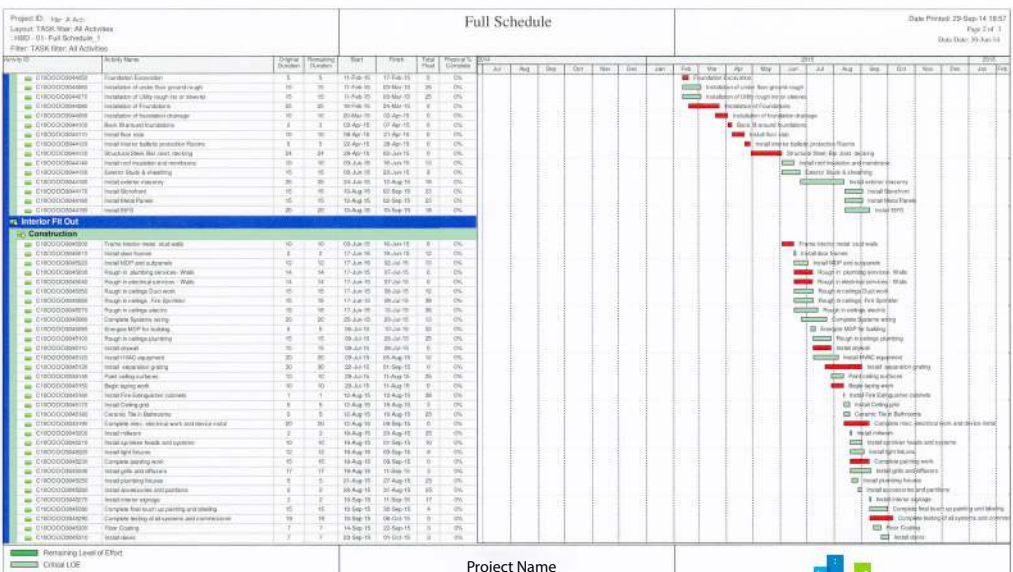
Full Schedule
Project ID: Ver. A Act
Layout: TASK filter: All Activities
: HBD - 01 - Full Schedule_1
Filter: TASK filter: All Activities
Date Printed: 29-Sep-14 18:57
Page 2 of 3
Data Date: 30-Jun-14
Activity ID
Activity Name
Original Duration
Remaining Duration
Start
Finish
Total Float
Physical % Complete
2014
2015
2016
Jul
Aug
Sep
Oct
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Dec
Jan
Feb
C1800OOD0944650 Foundation Excavation 5 5 11-Feb-15 17-Feb-15 0 0%
C1800OOD0944660 Installation of under floor ground rough 15 15 11-Feb-15 03-Mar-15 26 0%
C1800OOD0944670 Installation of Utility rough ins or sleeves 15 15 11-Feb-15 03-Mar-15 25 0%
C1800OOD0944680 Installation of Foundations 20 20 18-Feb-15 24-Mar-15 6 0%
C1800OOD0944690 Installation of foundation drainage 10 10 23-Mar-15 02-Apr-15 6 0%
C1800OOD0944700 Back fill around foundations 3 3 03-Apr-15 07-Apr-15 6 0%
C1800OOD0944710 Install floor slab 10 10 08-Apr-15 21-Apr-15 6 0%
C1800OOD0944720 Install interior bulkhead protection Rooms 5 5 22-Apr-15 28-Apr-15 0 0%
C1800OOD0944730 Structural Steel, Bar Joist, decking 24 24 29-Apr-15 03-Jun-15 0 0%
C1800OOD0944740 Install roof insulation and membrane 10 10 05-Jun-15 16-Jun-15 10 0%
C1800OOD0944750 Exterior Studs & sheathing 15 15 05-Jun-15 23-Jun-15 8 0%
C1800OOD0944760 Install exterior masonry 35 35 24-Jun-15 12-Aug-15 16 0%
C1800OOD0944770 Install Storefront 15 15 13-Aug-15 03-Sep-15 23 0%
C1800OOD0944780 Install Metal Panels 15 15 13-Aug-15 02-Sep-15 23 0%
C1800OOD0944790 Install RPR 20 20 13-Aug-15 10-Sep-15 18 0%
Interior Fit Out
Construction
C1800OOD0945000 Frame Interior metal stud walls 10 10 03-Jun-15 16-Jun-15 6 0%
C1800OOD0945010 Install steel frames 5 5 17-Jun-15 23-Jun-15 12 0%
C1800OOD0945020 Install MEP and subpanels 12 12 17-Jun-15 02-Jul-15 13 0%
C1800OOD0945030 Rough in plumbing services - Walls 14 14 17-Jun-15 07-Jul-15 6 0%
C1800OOD0945040 Rough in electrical services - Walls 14 14 17-Jun-15 07-Jul-15 6 0%
C1800OOD0945050 Rough in ceilings Duct work 15 15 17-Jun-15 09-Jul-15 10 0%
C1800OOD0945060 Rough in ceilings Fire Sprinkler 15 15 17-Jun-15 09-Jul-15 39 0%
C1800OOD0945070 Rough in ceilings electric 15 15 17-Jun-15 15-Jul-15 36 0%
C1800OOD0945080 Complete Systems wiring 20 20 25-Jun-15 23-Jul-15 13 0%
C1800OOD0945090 Energize MDP for building 5 5 06-Jul-15 10-Jul-15 32 0%
C1800OOD0945100 Rough in ceilings plumbing 15 15 09-Jul-15 29-Jul-15 25 0%
C1800OOD0945110 Install drywall 15 15 09-Jul-15 29-Jul-15 6 0%
C1800OOD0945120 Install HVAC equipment 20 20 09-Jul-15 05-Aug-15 10 0%
C1800OOD0945130 Install separation grating 30 30 22-Jul-15 01-Sep-15 0 0%
C1800OOD0945140 Paint ceiling surfaces 10 10 29-Jul-15 11-Aug-15 25 0%
C1800OOD0945150 Begin taping work 10 10 29-Jul-15 11-Aug-15 0 0%
C1800OOD0945160 Install Fire Extinguisher cabinets 1 1 12-Aug-15 12-Aug-15 89 0%
C1800OOD0945170 Install Ceiling grid 5 5 12-Aug-15 18-Aug-15 0 0%
C1800OOD0945180 Ceramic Tile in Bathrooms 5 5 12-Aug-15 18-Aug-15 23 0%
C1800OOD0945190 Complete misc. electrical work and device instal 20 20 12-Aug-15 08-Sep-15 0 0%
C1800OOD0945200 Install millwork 2 2 13-Aug-15 14-Aug-15 23 0%
C1800OOD0945210 Install sprinkler heads and systems 10 10 19-Aug-15 01-Sep-15 10 0%
C1800OOD0945220 Install light fixtures 10 10 19-Aug-15 03-Sep-15 9 0%
C1800OOD0945230 Complete painting work 15 15 19-Aug-15 03-Sep-15 0 0%
C1800OOD0945240 Install grills and diffusers 17 17 19-Aug-15 11-Sep-15 3 0%
C1800OOD0945250 Install plumbing fixtures 5 5 31-Aug-15 07-Aug-15 25 0%
C1800OOD0945260 Install accessories and partitions 5 5 08-Aug-15 31-Aug-15 25 0%
C1800OOD0945270 Install interior signage 3 3 10-Sep-15 11-Sep-15 17 0%
C1800OOD0945280 Complete final touch up painting and labeling 15 15 10-Sep-15 30-Sep-15 4 0%
C1800OOD0945290 Complete testing of all systems and commissione 19 19 10-Sep-15 06-Oct-15 4 0%
C1800OOD0945300 Floor Coating 7 7 14-Sep-15 22-Sep-15 3 0%
C1800OOD0945310 Install doors 7 7 23-Sep-15 01-Oct-15 3 0%
Remaining Level of Effort
Critical LOE
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Project Name
More Detail About Project
Contract No. 123456789
NEXTbuild
